

A stylized graphic of a road with a dashed white line down the center, receding into the distance. Above the road are several concentric circles, suggesting a horizon or a signal.

# Transportation Sales Tax Program

## **OCST Update**

**July 13, 2026**



# Sales Tax Program Overview



## Referendums

Each approved for a period of 7 years

- 2008 (May 2009 - April 2016)
- 2014 (May 2016 - April 2023)
- 2022 (May 2023 - April 2030)



## Funds Collected with Interest

- 2008 - \$143.7 million
- 2014 - \$274.5 million
- 2022 - \$587 million (estimated)



## Capacity Projects

### Intersection Projects

### Other Transportation Projects

### Dirt to Pave Projects

### Resurfacing Projects

### Greenbelt Projects

# Recently Completed Projects

## Henry Brown Boulevard Extension Phase 1A (Red Bank Road & Henry Brown Boulevard)

District 1 | 2008 Capacity Project

- \$2.8 million (All Sales Tax)
- Managed by SCDOT
- Construction contract awarded September 2024 / Contract completion date June 2026
- Substantial Completion was issued June 30, 2026.



US 176  
Phase 1

## US 176 Widening Phase 1 (US 17A to Nexton Parkway)

District 5 & 6 | 2014 Capacity Project

- \$65.3 million (All Sales Tax)
- Managed by Berkeley Count
- Construction contract awarded August 31, 2021 / Contract completion date November 14, 2025
- Substantial Completion was issued December 23, 2025.



United Drive

## United Drive (5 miles SE of SC 41 to Halfway Creek Road S-100)

District 8 | 2022 Major Resurfacing

- \$1 million (All Sales Tax)
- Managed by Berkeley County
- The 2.56 miles were resurfaced as part of the 2024 Local Resurfacing Package.

# Projects Under Construction

## 2024 Local Resurfacing

All Districts | 2022 Local Resurfacing

- \$12.17 million (All Sales Tax)
- Managed by Berkeley County, 33 miles
- Construction Notice to Proceed March 10, 2025 / Contract completion date September 2026
- 96 of 98 roads have been resurfaced through June 30, 2026.

## 2025 Local Resurfacing

All Districts | 2022 Local Resurfacing

- \$8.90 million (All Sales Tax)
- Managed by Berkeley County, 25.86 miles
- Construction Notice to Proceed April 13, 2026 / Contract completion date December 2026
- 11 of 54 roads have been resurfaced through June 30, 2026.

## 2026 Local Resurfacing Package

Various Districts | 2022 Local Resurfacing

- \$12.10 million (All Sales Tax)
- Managed by Berkeley County, 30.53 miles
- Preconstruction Meeting will be held July 16, 2026.

Over

89

**Miles Under Contract to  
for Resurfacing**

# Projects Under Construction

## Sangaree Parkway Improvements

District 4 | 2022 Other Transportation Project

- \$170k (All Sales Tax)
- Managed by Berkeley County
- Construction Notice to Proceed July 6, 2026 / Contract completion date November 2026
- Construction of the left-turn lanes and median end treatments is underway.



# 2024 OCST Resurfacing

Box Turtle Court



Before



After

Cainhoy Village Road




Before



After

Fort Drive

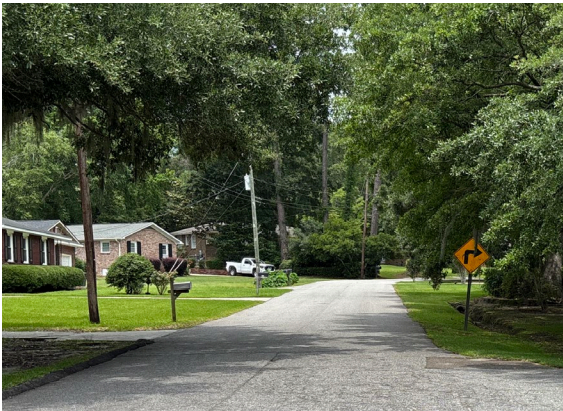

Before



After

Lyle Road



Before



After



# 2025 OCST Resurfacing

Blue King Drive



Before



After

Helmet Avenue



Before



After

# Projects In Design - Capacity

## Cypress Gardens Road Improvements

District 3 | 2022 Capacity Project

*Construction anticipated 4<sup>th</sup> Quarter 2027*

- Preliminary plans are underway for the intersection of Cypress Gardens Rd and Pimlico Boulevard.

## Jedburg Road Improvements Phase 1 (County Line to Wildgame Road)

District 7 | 2022 Capacity Project

*Construction anticipated 4<sup>th</sup> Quarter 2028*

- Right of way acquisition is underway for the Dawson Branch Road realignment.
- Final design is underway for the Strathmore Road realignment.
- Right-of-Way plans are underway for the Jedburg Road mainline improvements.
- Submitted for the USDOT BUILD Grant in February.

## Jedburg Road Improvements Phase 2 (Realignment of Jedburg Rd to US 176)

District 7 | 2022 Capacity Project

*Construction anticipated 4<sup>th</sup> Quarter 2027*

- Preliminary plans are underway.
- Advanced right of way acquisition is underway for the realignment of Jedburg Rd into US 176 at Black Tom Road.

## North Cedar Street Extension

District 7 | 2022 Capacity Project

- Traffic study is being finalized.



Jedburg Road  
Phase1



# Projects In Design - Capacity

## Old Mount Holly Road Improvements

District 3 | 2022 Capacity Project

*Construction anticipated 4<sup>th</sup> Quarter 2028*

- Right-of-Way plans are underway.
- CHATS provided \$500,000 from the Regional Mobility Program for this project.

## US 176 Widening Phase 2 (Nexton Parkway to Jedburg Road)

District 5 & 7 | 2022 Capacity Project

*Construction anticipated 3<sup>rd</sup> Quarter 2028*

- Public Meeting was held January 29, 2026.
  - 68 people signed in at the meeting
  - 1,200 Public Meeting Website views (1/29/26-3/1/26)
  - 215 comments received
- Right-of-Way plans are underway.
- Project was awarded \$22.5M through the USDOT BUILD.

## US 52 and US 176 (Short Term)

District 3 | 2022 Capacity Project

*Construction anticipated 1<sup>st</sup> Quarter 2027 (Phase 1)*

- Right-of-Way acquisition is underway for Phase 1.
- Final construction plans for Phase 1 are under review.
- Right-of-Way plans for Phase 2 are under review.



Old Mount Holly  
Road



US 176  
Phase 2

# Projects In Design - Capacity

## US 52 and US 176 (Long Term)

District 3 | 2022 Capacity Project

- Notice to Proceed was issued May 2026
- Environmental studies are underway.

## US 52 Corridor Improvements

District 3, 6, 7 & 8 | 2022 Capacity Project

- The traffic study and phasing plan have been completed.



US 52 and US 176

# Projects In Design – Intersection

## Black Tom Road at Black Tom Road Extension

District 7 | 2022 Intersection Project

*Construction anticipated 4<sup>th</sup> Quarter 2027*

- Public Meeting was held March 26, 2026.
  - 22 people signed in at the meeting
  - 109 Public Meeting Website views (March 2026)
  - 14 comments received
- Right-of-way plans have been submitted and are under review.
- CHATS provided \$3.8M from the Rural Mobility Program for this project.

## Cooper Store Road at Black Tom Road Extension

District 7 | 2022 Intersection Project

*Construction anticipated 4<sup>th</sup> Quarter 2027*

- Public Meeting was held March 26, 2026.
  - 22 people signed in at the meeting
  - 109 Public Meeting Website views (March 2026)
  - 14 comments received
- Right-of-way plans have been submitted and are under review.
- CHATS provided \$2.5M from the Rural Mobility Program for this project.



Cooper Store Road at  
Black Tom Road Extension



# Projects In Design – Intersection

## River Landing Drive at Seven Farms Drive

District 2 | 2022 Intersection Project

*Construction anticipated 3<sup>rd</sup> Quarter 2026*

- Bid opening is July 14, 2026 and bid will go to County Council for award July 27, 2026.

## Royle Road at Farmington Road / Treeland Drive

District 4 | 2022 Intersection Project

*Construction anticipated 1<sup>st</sup> Quarter 2027*

- Public Meeting was held January 15, 2026.
  - 63 people signed in at the meeting
  - 3,422 Public Meeting Website views (12/31/25-01/30/2026)
  - 42 comments received
- Right-of-way plans have been submitted and are under review.
- CHATS provided \$500,000 from the Regional Mobility Program for this project.

## Snake Road at NAD Road

District 1 | 2022 Intersection Project

*Construction anticipated 3<sup>rd</sup> Quarter 2027*

- Right of way plans are underway.



River Landing at  
Seven Farms Drive



Snake Road at  
NAD Road

# Projects In Design – Intersection

## Tanner Ford Boulevard at Tanner Hall Boulevard

District 2 | 2022 Intersection Project

Construction anticipated 1<sup>st</sup> Quarter 2027

- Right-of-Way Acquisition is underway.
- Final construction plans are underway.

## US 52 at Old 52 and Rembert C. Dennis Boulevard

District 6 & 8 | 2022 Intersection Project

Construction anticipated 4<sup>th</sup> Quarter 2027

- Preliminary design is underway.

## US 52 at southern terminus of Old 52

District 3 & 8 | 2022 Intersection Project

Construction anticipated 4<sup>th</sup> Quarter 2027

- Notice to Proceed was issued July 2026
- Preliminary design is underway.

## US 52 at Stephanie Drive and Windsor Mill Road

District 3 | 2022 Intersection Project

Construction anticipated 3<sup>rd</sup> Quarter 2027

- Right-of-Way plans are underway.



US 52 at Old 52 and  
Rembert C. Dennis Boulevard



US 52 at Stephanie Drive  
and Windsor Mill Road

# Projects In Design – Other Transportation

## Clements Ferry Road Phase 1 Multi-Use Path

District 2 | 2022 Other Transportation Project  
*Construction anticipated 4<sup>th</sup> Quarter 2026*

- Construction documents are under review by SCDOT.

## Old Highway 52 at Colony Post Loop and Cypress Plantation Road

District 3 | 2022 Other Transportation Project  
*Construction anticipated 3<sup>rd</sup> Quarter 2026*

- Bid opening is July 14, 2026 and bid will go to County Council for award July 27, 2026.

## Old Highway 52 at Orion Way

District 2 | 2022 Other Transportation Project  
*Construction anticipated 3<sup>rd</sup> Quarter 2026*

- Bid opening is July 14, 2026 and bid will go to County Council for award July 27, 2026.

## Oxford and Trinity Bridges

District 4 | 2022 Other Transportation Project

- Preliminary roadway and bridge plans have been reviewed and additional analysis performed to determine the necessary improvements.



Oxford Bridge



Trinity Bridge



# Projects In Design – Other Transportation

## River Reach Drive

District 2 | 2022 Other Transportation Project

- The improvements are proposed to be completed as part of a DR Horton project. DR Horton is currently working through the City of Charleston's permitting process.

## Sangaree Parkway Improvements

District 4 | 2022 Other Transportation Project

- Construction of the left-turn lanes and median end treatments is underway.
- Preliminary plans for multi-use path are underway.

## Yeamans Hall Road Improvements

District 1 | 2022 Other Transportation Project

- The County is partnering with the City of Hanahan to fund a portion of future improvements.
- Traffic report is under review.



Sangaree Parkway

# Projects In Design – Major Resurfacing

## **Bushy Park Road**

District 1, 2 & 8 | 2022 Major Resurfacing

- Berkeley County provided a Match Commitment Letter for the SCDOT's application to the Economic Development Administration (EDA) FY Disaster Supplemental Grant Project February 25, 2026.

## **Gravel Hill Road**

District 6 & 8 | 2022 Major Resurfacing

- Project is currently being evaluated.

## **SC 45**

District 7 & 8 | 2022 Major Resurfacing

- Project is currently being evaluated.

## **Harristown Road**

District 6 & 8 | 2022 Major Resurfacing

- Project is currently being evaluated.

# Projects In Design – Local Resurfacing

## County and City Roads Pavement Evaluation

Various Districts | 2022 Resurfacing

- All County and City roads will be re-evaluated 4<sup>th</sup> Quarter 2026.

## 2027 Local Resurfacing Package

Various Districts | 2022 Local Resurfacing

- Bid package will be prepared 3<sup>rd</sup> Quarter 2026.



# Projects In Design – Dirt to Pave

## **Benjamin Drive**

District 8 | 2008 Dirt to Pave

*Construction anticipated 3<sup>rd</sup> Quarter 2026*

- Bid opening is July 14, 2026 and bid will go to County Council for award July 27, 2026.

## **Collins Hill Drive**

District 2 | 2014 Dirt to Pave

*Construction anticipated 3<sup>rd</sup> Quarter 2026*

- Bid opening is July 14, 2026 and bid will go to County Council for award July 27, 2026.

## **Constitution Avenue**

District 8 | 2014 Dirt to Pave

*Construction anticipated 3<sup>rd</sup> Quarter 2026*

- Bid opening is July 14, 2026 and bid will go to County Council for award July 27, 2026.

## **Rice Hope Roads (Childsbury Drive, Crawdad Court, Osprey Drive, View Drive)**

District 4 | 2014 Dirt to Pave

*Construction anticipated 3<sup>rd</sup> Quarter 2026*

- Bid opening is July 14, 2026 and bid will go to County Council for award July 27, 2026.

# Projects In Design – Dirt to Pave

## **Strawberry Roads (Arquat Lane, Berry Road, Christ Temple Road, Junior Road, Oaklawn Drive, Rebecca Lane, Tigers Den Lane)**

District 4 | 2014 Dirt to Pave

*Construction anticipated 3<sup>rd</sup> Quarter 2026*

- Bid opening is July 14, 2026 and bid will go to County Council for award July 27, 2026.

# Projects In Design – 2022 Dirt to Pave

| Road Name                                              | District | Paving                      | Chip Seal                               | Other                     |
|--------------------------------------------------------|----------|-----------------------------|-----------------------------------------|---------------------------|
| Bo Cat Alley                                           | 8        |                             | Will be completed with in-house forces. |                           |
| Dennis Ridge Road<br>(Mandella Road to Lightning Lane) | 7        | Preliminary plans underway. |                                         |                           |
| George Street                                          | 8        |                             |                                         | Project scoping underway. |
| Hammond Street                                         | 6        |                             | Will be completed with in-house forces. |                           |
| Hill Top Drive                                         | 6        |                             | Will be completed with in-house forces. |                           |
| Judy Hill Drive                                        | 4        | Preliminary plans underway. |                                         |                           |
| Richardson Street                                      | 6        |                             | Will be completed with in-house forces. |                           |
| Seabrook Drive                                         | 4        |                             | Will be completed with in-house forces. |                           |
| St Julian Drive                                        | 7        | Preliminary plans underway. |                                         |                           |
| Webb Street                                            | 6        |                             | Will be completed with in-house forces. |                           |



# Completed Projects

## Capacity Projects (~\$318M spent)

- Clements Ferry Rd Improvements Phase 1 (I-526 to Jack Primus Road) (2008)
- Clements Ferry Rd Improvements Phase 2 (Jack Primus Road to SC 41) (2014)
- College Park Rd Improvements (2008)
- Henry Brown Blvd Extension Phase 1 (Liberty Hall Road to Red Bank Road) (2008)
- Henry Brown Blvd Extension Phase 1A Red Bank Road & Henry Brown Boulevard) (2008)
- Henry Brown Blvd Extension Phase 2 (Liberty Hall Road to US 52) (2014)
- Jedburg Rd Interchange (2014)
- Nexton Parkway (Pine Hollow Drive to US 176) (2014)
- Railroad Ave Extension (2008)
- Sheep Island (Nexton) Interchange & I-26 Widening (2014)
- Sheep Island (Nexton) Parkway South (I-26 to North Maple Street) (2014)
- US 176 Phase 1 (2014)
- US Highway 17-A Improvements (2008)



Sheep Island (Nexton) Parkway  
& I-26 Widening



US 176 Phase 1

# Completed Projects

## Intersection Projects (~\$13 M spent)

Daniel Island Drive at Seven Farms Drive (2014)  
Foster Creek Road at Tanner Ford Boulevard (2014)  
Henry Brown Boulevard at Tanner Ford Boulevard (2008)  
Highland Park Avenue at Hanahan Road (2008)  
Murray Drive at Yeamans Hall Road (2014)  
North Highway 17-A at Highway 41 (2008)  
Old Highway 52 at Cypress Gardens Road (2008)  
Royle Road at Sangaree Parkway (2014)



Daniel Island Drive at  
Seven Farms Drive



Royle Road at  
Sangaree Parkway

# Completed Projects

## Other Transportation Projects (~\$6M spent)

Berkeley County Airport Runway Extension Project (2014)  
Bushy Park Channel Dredging (2014)

## Major Resurfacing Projects (~\$32M spent)

Black Tom Road (2014)  
Dr. Evans Road (2014)  
Hoodtown Road (2014)  
Jedburg Road (US 176 to County Line) (2008)  
Mudville Road (2014)  
Old Highway 52 (2014)  
SC 402 (minimum of 7 miles) (2014)  
SC 45 (minimum of 6 miles) (2014)  
SC 6 (Main St. Moncks Corner) (2014)  
SC Highway 6 (S-5 to SC-311) (2008)  
United Drive (5 miles SE of SC 41 to Halfway Creek Road S-100) (2022)



Bushy Park  
Channel Dredging





# Completed Projects – Local Resurfacing (107 Roads, ~\$9.4M spent)

Amberside Drive (2022)  
Autumn Lane (2022)  
Baldwin Lane (2022)  
Balmoral Circle (2022)  
Belleplaine Drive (2022)  
Blue King Avenue (2022)  
Box Turtle Court (2022)  
Braeford Court (2022)  
Cable Court (2022)  
Cable Drive (2022)  
Caboose Court (2022)  
Cainhoy Village Road (2022)  
Cairnwell Pass (2022)  
Calamus Pond Road (2022)  
Candleberry Circle (2022)  
Cannon Avenue (2022)  
Carlisle Bay Court (2022)  
Carter Drive (2022)  
Castlecombe Court (2022)  
Churchill Road (2022)  
Coachman Lane (2022)  
College Drive (2022)  
Colonel Maham Drive (2022)  
Conductor Court (2022)  
Conset Bay Court (2022)  
Creek Stone Way (2022)

Crossbill Trail (2022)  
Cross Tie Court (2022)  
Cuthbery Drive (2022)  
Dundalk Court (2022)  
Eight Point Road (2022)  
Expressway Drive (2022)  
Fairchild Street (2022)  
Farrell Street (2022)  
Fort Drive (2022)  
Hastie Drive (2022)  
Hawks Circle (2022)  
Helmet Avenue (2022)  
Hill Court (2022)  
Homer Drive (2022)  
Hopper Drive (2022)  
Indigo Lane (2022)  
Iron Court (2022)  
Iron Road (2022)  
Island Park Roundabout (2022)  
Judy Hill Drive (2022)  
Kingsbridge Drive (2022)  
Kitridge Point (2022)  
Lauren Lane (2022)  
Loganberry Circle (2022)  
Long Bay Court (2022)  
Long Needle Drive (2022)

Lowndes Road (2022)  
Lyle Road (2022)  
Mallory Drive (2022)  
Mano Street (2022)  
Maywood Drive (2022)  
Messina Street (2022)  
Monsarret Lane (2022)  
Mookees Lane (2022)  
Moorchester Court (2022)  
Mustang Circle (2022)  
Nelliefield Creek Drive (2022)  
Newell Drive (2022)  
Newell Street (2022)  
North Mano Street (2022)  
Nyler Court (2022)  
Palm Street (2022)  
Pearle Street (2022)  
Pine Street (2022)  
Prospect Way (2022)  
Pullman Avenue (2022)  
Rail Drive (2022)  
Redeemer Drive (2022)  
River Landing Drive (2022)  
Sapling Court (2022)  
Sapling Drive (2022)  
Shoreside Court (2022)



Dundalk Court



Lowndes Road




# Completed Projects – Local Resurfacing (107 Roads, ~\$9.4M spent)

Silver King Avenue (2022)  
Song Sparrow Way (2022)  
South Basilica Avenue (2022)  
South Pembroke Drive (2022)  
Speightstown Court (2022)  
Spring Hall Drive (2022)  
Stonehurst Drive (2022)  
Sterling Oaks (2022)  
Sturges Court (2022)  
Summerton Court (2022)  
Surrey Drive (2022)  
Tall Spruce Drive (2022)  
Trailway Drive (2022)  
Tram Boulevard (2022)  
Tram Court (2022)  
Travis Hill Road (2022)  
Turnbury Road (2022)  
Unity Rd (2022)  
W. Hartwick Lane (2022)  
Waddington Trace (2022)  
Wedgewood Drive (2022)  
Westward Drive (2022)  
Whisper Way (2022)  
Willard Drive (2022)  
Williams Court (2022)  
Woodsage Drive (2022)

Woodside Drive (2022)  
Yales Drive (2022)



Stonehurst Drive

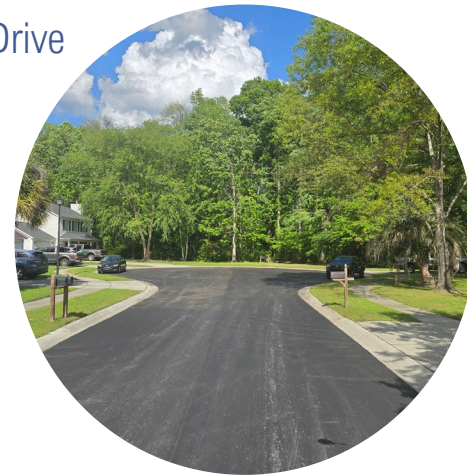

W Hartwick Lane

# Completed Projects – Dirt to Pave (73 Roads, ~\$25M spent)


Ambassador Avenue (2008)  
Arthur Gillins Lane (2008)  
Avery Drive (2008)  
Ballentine Street (2014)  
Barnyard Road (2014)  
Beulah Tabernacle Road (2008)  
Blanding Road (2008)  
Bridle Lane (2014)  
Britt Drive (2014)  
Calestown Road (2008)  
Cannon Court (2014)  
Caroline Drive (2014)  
Cherrywood Drive (2014)  
Churchill Road (2014)  
Coaxum Road (2008)  
Countryside Way (2014)  
Crawford Road (2008)  
Crest Lane (2014)  
Dennis Drive (2008)  
Dewey Drive (2014)  
England Road (2008)  
Fall Street (2014)  
Farm Hill Circle (2008)  
Fauling Road (2008)  
Felix Lane (2014)

Fennick Drive (2008)  
Firehouse Road (2008)  
Four Acre Lane (2014)  
Frances Street (2014)  
Galloway Court (2014)  
George Wigfall Road (2008)  
Georgiana Drive (2014)  
Green Bay Road (2008)  
Greenleaf Drive (2014)  
Harlock Drive (2014)  
Heyward Lane (2014)  
Hunt Drive (2014)  
Jacob Piland Road (2008)  
Jasper Lane (2014)  
Jelly Rolls Road (2014)  
Kale Street (2014)  
Marvel Oak Circle (2014)  
Mary Street (2014)  
McElveen Avenue (2014)  
Memory Lane (2014)  
Millwood Loop (2014)  
Mitchum Town Road (2008)  
Morrison Drive (2014)  
Moultrie Lane (2008)  
Mourning Dove Court (2008)

Old Parker Road (2014)  
Orvin Street (2014)  
Paslay Drive (2014)  
Radford Lane (2014)  
Ranch Drive (2014)  
Sanders McNeil Road (2014)  
Schurlknight Road (2014)  
Sheriff's Lane (2014)  
Spring Pond Road (2008)  
Starks Croker Drive (2008)  
Steelshed Lane (2014)  
Stevensridge Lane (2008)  
Striper Avenue (2014)  
Telfair Road (2014)  
Timberline Way (2008)  
Tobacco Road (2008)  
Tom Conley Park Road (2014)  
Tracy Road (2014)  
Tuxbury Farm Road (2014)  
Upton Road (2014)  
Water Pointe Avenue (2014)  
Wilder Road (2008)  
Zion Road (2008)



Starks Croker

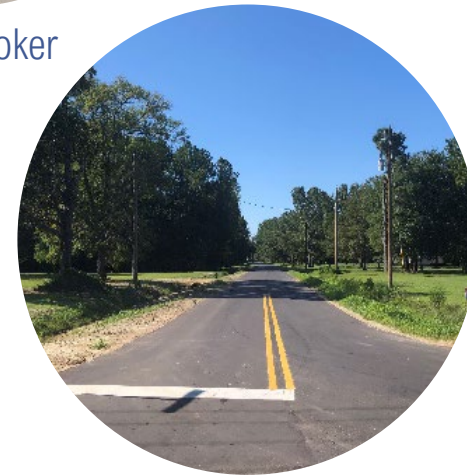

Jacob Piland

# Building Berkeley

Learn more about active infrastructure improvements around Berkeley County including bridges, dirt to pave, interchanges, resurfacing, storm water, and road widening road projects by using the **QR Code** below or going to **[buildingberkeley.com](https://buildingberkeley.com)**!



# Thank You

To access this presentation, use the QR Code below!

